


Addington Track Remediation Works

UPDATE : Week 2

Monday 01 July - Saturday 06 July 2024

This Week

- surveyor onsite - survey of existing basecourse & design model for reinstatement
- ongoing sieving of clean reusable sand
- all construction materials delivered & onsite
- reinstatement of basecourse to new GPS design model
- compaction of basecourse
- decommissioning of 520m power & starting boxes
- removal of 520m start concrete slab
- removal & modification to existing 520m shelter
- installation of new conduits & trip starts
- sand testing of stockpiled track sand

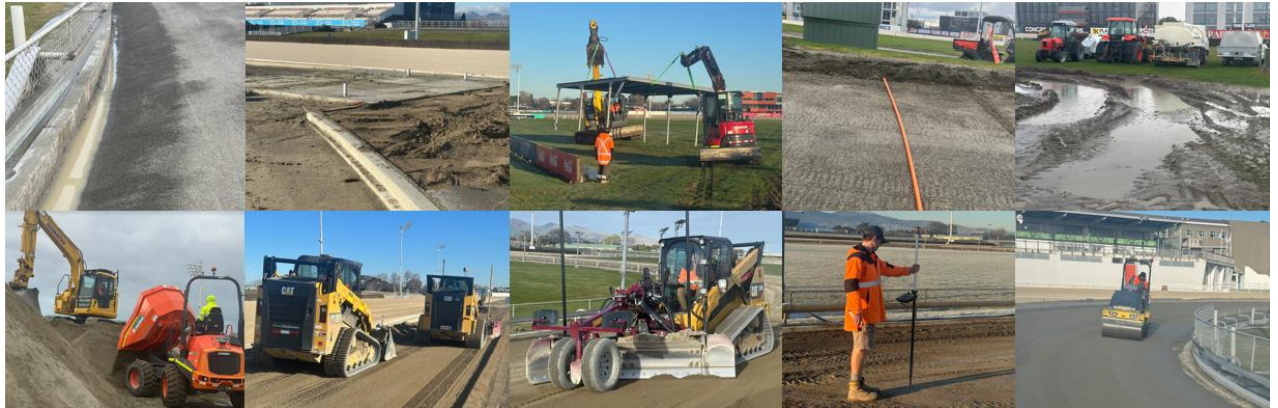

This Coming Week

- surveyor on track Monday/Tuesday - final basecourse survey (as built)(HOLD POINT)
- installation of new sections of outer concrete edge/plinth
- formwork & installation of new concrete slab for new 525m start
- delivery of geofabric
- installation of new perimeter profile drain
- removal of contaminated sand and geofabric for dumping offsite
- removal of concrete & asphalt for dumping offsite
- placement of new geofabric layer
- reinstatement of track sand to new design grades & levels

